



DEPARTMENT OF ENGINEERING AND PLANNING  
Division of Engineering  
One Spring Street  
Newton, New Jersey 07860  
973-579-0430  
[dpw@sussex.nj.us](mailto:dpw@sussex.nj.us)  
John C. Risko, P.E., P.L.S., P.P.  
Division Director/Assistant County Engineer

## **Project Status – Bridge E-07 (Franklin Viaduct) Distributed: January 4, 2013**

### **Project:**

#### **Replacement of Sussex County Bridge E-07**

Carrying County Route 631 (North Church Road) over Walkkill River and New York Susquehanna & Western Railroad

**Designer:** Cherry, Weber and Associates

**Contractor:** Awarded to Ritacco Construction, Inc., of Belleville, NJ for \$8,174,000.00

### **Schedule:**

Bridge superstructure demolition is 50% complete.  
Foundation construction to begin in mid-winter.  
Construction Completion Date: December 31, 2013

**BRIDGE DEMOLITION PROGRESSING**  
**STEEL FABRICATION DRAWINGS IN REVIEW**



### **Construction Activities:**

- ✓ Implement road closure and detour
- Demolition of bridge superstructure and ramp
- Demolition of substructure, abutments and footings
- Installation of sheeting and piles
- Placement of reinforced concrete footings, abutments, wing walls and bridge piers
- Installation of deck beams
- Construction of reinforced concrete deck
- Construction of reinforced concrete bridge sidewalk and parapets
- Installation of bridge railing and lighting
- Placement of backfill and drainage structures
- Construction of reinforced concrete approach slabs
- Roadway paving and striping
- Installation of beam guide rail
- Topsoil, seed and landscaping




*For more information about this project please feel free to contact Charles Porter, P.E., at the Sussex County Division of Engineering at 973-579-0430 or [dpw@sussex.nj.us](mailto:dpw@sussex.nj.us)*



DEPARTMENT OF ENGINEERING AND PLANNING  
 Division of Engineering  
 One Spring Street  
 Newton, New Jersey 07860  
 973-579-0430  
[dpw@sussex.nj.us](mailto:dpw@sussex.nj.us)  
 John C. Risko, P.E., P.L.S., P.P.  
 Division Director/Assistant County Engineer

**Project Status – Bridge E-07 (Franklin Viaduct) Distributed: January 4, 2013**

*Future updates of the project schedule will be provided as dates and durations are confirmed.*

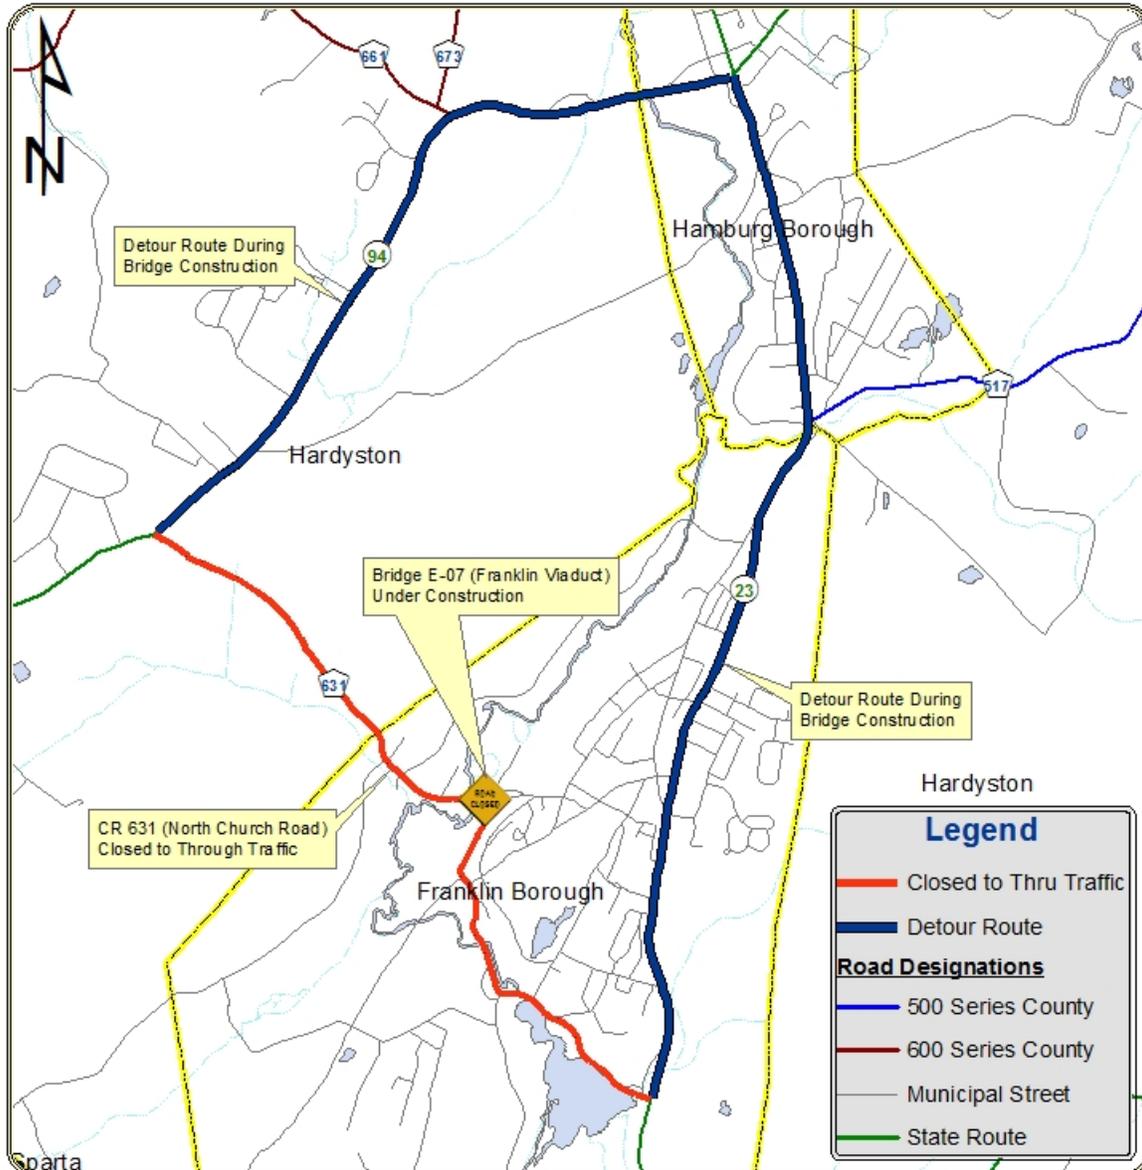

**PROJECT DETOUR MAP**
