



DEPARTMENT OF ENGINEERING AND PLANNING  
 Division of Engineering  
 One Spring Street  
 Newton, New Jersey 07860  
 973-579-0430  
[dpw@sussex.nj.us](mailto:dpw@sussex.nj.us)  
 Matthew R. Sinke, P.E.  
 Division Director/Assistant County Engineer

**Project Status – Bridge X-09 CR 565**

**Distributed: November 16, 2018**

**Project:**

**Reconstruction & Realignment of Bridge X-09**  
 Carrying County Route 565 over the Papakating Creek,  
 Wantage Township

**Designer:** Cherry, Weber & Associates, Freehold, NJ

**Contractor:** Awarded to Sparwick Contracting, Inc.,  
 Lafayette, NJ for \$3,599,825.00

**\*REVISED Construction Schedule:**

Contract Award: December 13, 2017  
 Road Closed for Construction: June 26, 2018

**Anticipated Completion & Road Opening: Summer 2019**

**\*Note – Construction has been delayed due to inclement weather & unanticipated subsurface conditions.**

**Construction Funding:**

|                          |                       |
|--------------------------|-----------------------|
| NJDOT 2015 LBFNP (TTF)   | \$1,000,000.00        |
| NJDOT 2016 LBFNP (TTF)   | \$ 500,000.00         |
| NJDOT 2017 LBFNP (TTF)   | \$1,000,000.00        |
| NJDOT 2018 LBFNP (TTF)   | \$ 900,000.00         |
| 2016/2017 County Capital | \$ 199,825.00         |
| <b>TOTAL</b>             | <b>\$3,599,825.00</b> |

**Construction Activities:**

- ✓ Implement Road Closure/Detour – **Complete**
- ✓ Install Soil Erosion & Sediment Control Measures – **Complete**
- ✓ Demolish Existing Structure – **Complete**
- ✓ Install Sheeting – **Complete**
- Construct Bridge Footings/Abutments/Wingwalls – **In Progress**
- Install Bearings/Erect Beams
- Construct Bridge Deck
- Construct Bridge Parapet & Rail
- Construct Retaining Walls – **In Progress**
- Construct Approach Roadway
- Install Pavement and Striping
- Install Guiderail
- Landscaping & Incidental Items of Work
- Reopen Roadway

For more information about this project please contact Susan Delmar, P.E., at the Sussex County Division of Engineering at 973-579-0430 or [dpw@sussex.nj.us](mailto:dpw@sussex.nj.us)



Demolition of South Abutment



Site Flooding After Heavy Rain



Tying North Abutment Reinforcing Steel




DEPARTMENT OF ENGINEERING AND PLANNING  
 Division of Engineering  
 One Spring Street  
 Newton, New Jersey 07860  
 973-579-0430  
[dpw@sussex.nj.us](mailto:dpw@sussex.nj.us)  
 Matthew R. Sinke, P.E.  
 Division Director/Assistant County Engineer

**Project Status – Bridge X-09 CR 565**

**Distributed: November 16, 2018**

**LOCATION MAP**

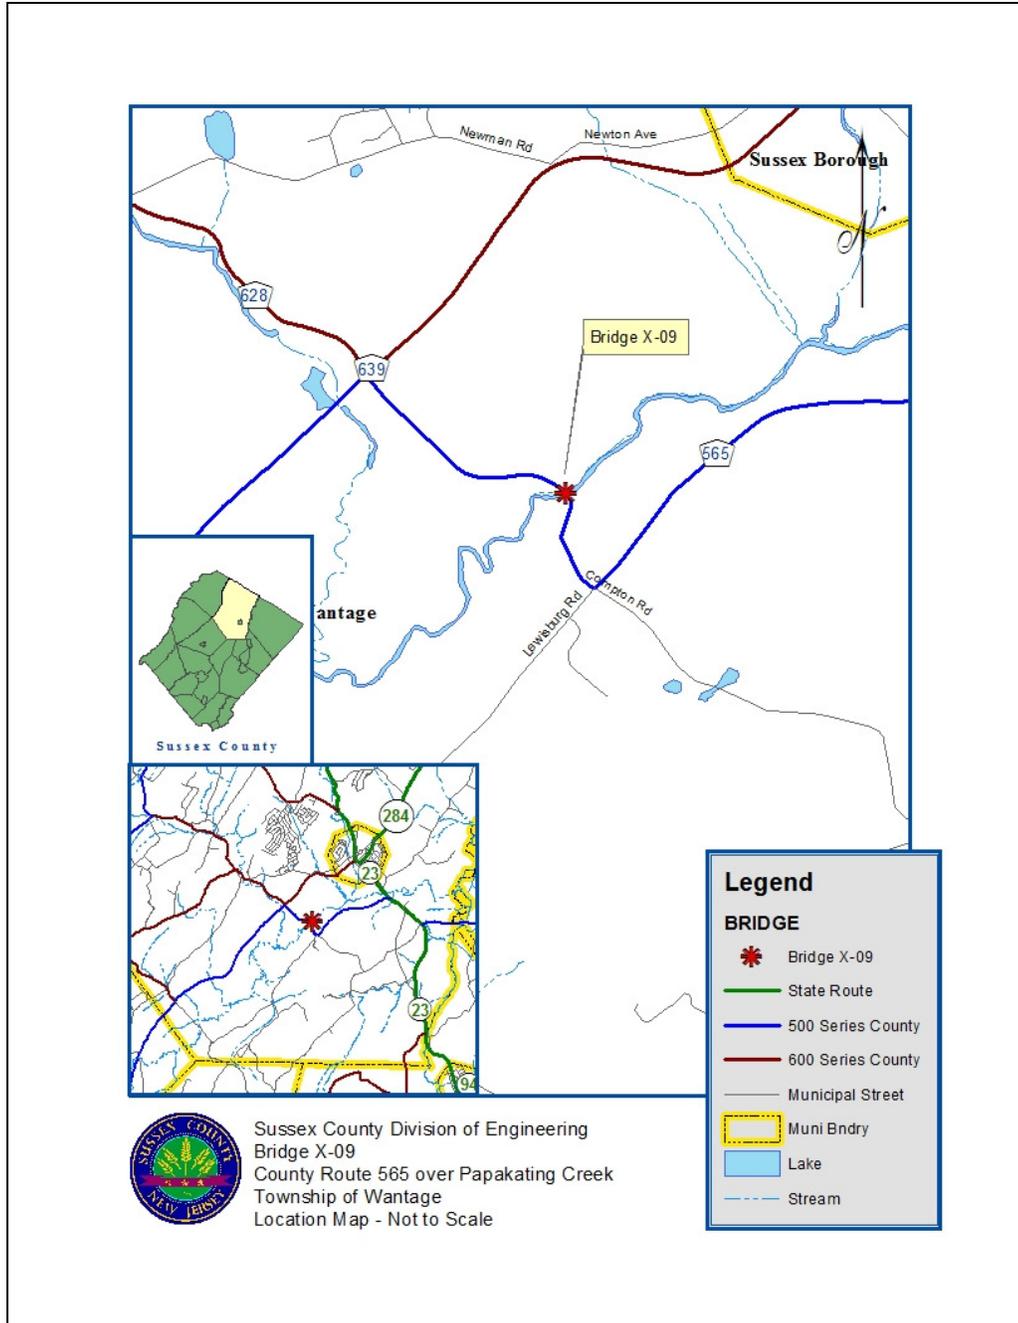



DEPARTMENT OF ENGINEERING AND PLANNING  
 Division of Engineering  
 One Spring Street  
 Newton, New Jersey 07860  
 973-579-0430  
[dpw@sussex.nj.us](mailto:dpw@sussex.nj.us)  
 Matthew R. Sinke, P.E.  
 Division Director/Assistant County Engineer

**Project Status – Bridge X-09 CR 565      Distributed: November 16, 2018**

**DETOUR MAP**

